



Valley Water

Clean Water • Healthy Environment • Flood Protection

Cunningham Flood Detention Facility Certification Project

Notice of Completion of Construction Contract

December 10, 2019


Presentation Topics

- Project Objective and Location
- Project Construction Costs
- Construction Photos

Project Objective

- The objective is to construct a floodwall and raise existing levee height to satisfy FEMA freeboard requirements.
- Other project elements include:
 - Construction of a new pedestrian pathway at the old trash compactor area.
 - Relocation of an existing trash compactor.
 - Riparian and city mitigation planting.
 - In-kind replacement of the existing chain link fence, and regrading trails.

Project Location

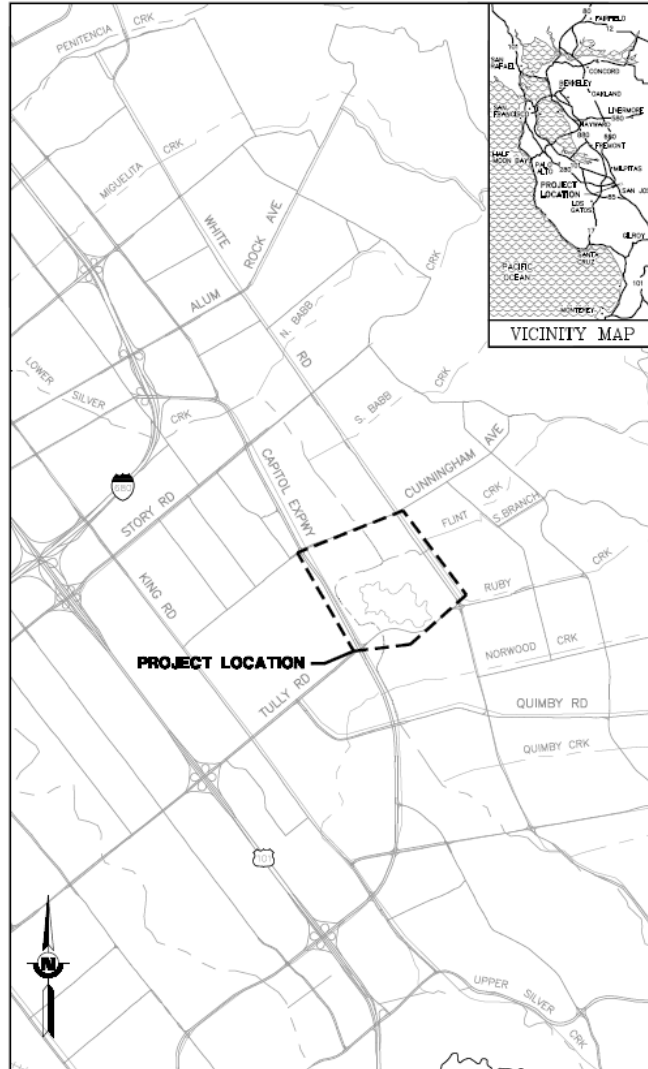

Presentation Topics

- Project Objective and Location
- Project Construction Costs
- Construction Photos

Project Costs

➤ Construction

- \$3,748,000.00 – Contract Award Amount
- \$574,791.63 – Contract Change Orders
- \$4,322,791.63 – Final Contract Amount
(15.3% increase)

➤ Funding Sources:

- Department of Water Resources Proposition 1E
- United States Department of Agriculture - Natural Resources Conservation Services

Presentation Topics

- Project Objective and Location
- Project Construction Costs
- Construction Photos

Construction Photos



BEFORE



08.23.2018 13:07

Flood Wall Along
Cunningham Ave.



10.01.2018 08:34



AFTER

Construction Photos



Levee Fill Along
Cunningham Ave.



Construction Photos



BEFORE

New Trail Pathway / Old Trash
Compactor Area



AFTER

Construction Photos



New Trash Compactor Area



Construction Photos



Final Mitigation Planting Area



THIS PAGE INTENTIONALLY LEFT BLANK
