

Infrastructure Reliability Portfolio 2 (IRP2) Water Treatment Plant Operations Building Seismic Retrofit Project

Notice of Completion of Construction Contract

August 9, 2016



Presentation Topics

- ▶ Project Description, Objective, and Location
- ▶ Project Construction Costs
- ▶ Construction Photos




Project Description and Objective

- ▶ Seismically retrofit the control building at the Rinconada Water Treatment Plant, Vasona Meter Shop and the Vasona Pump Station to meet life-safety criteria.
- ▶ Provides additional staff space, modernized building components, and improved plant operations



Project Location

Rinconada Water Treatment Plant & Vasona Pump Station – Los Gatos, Ca

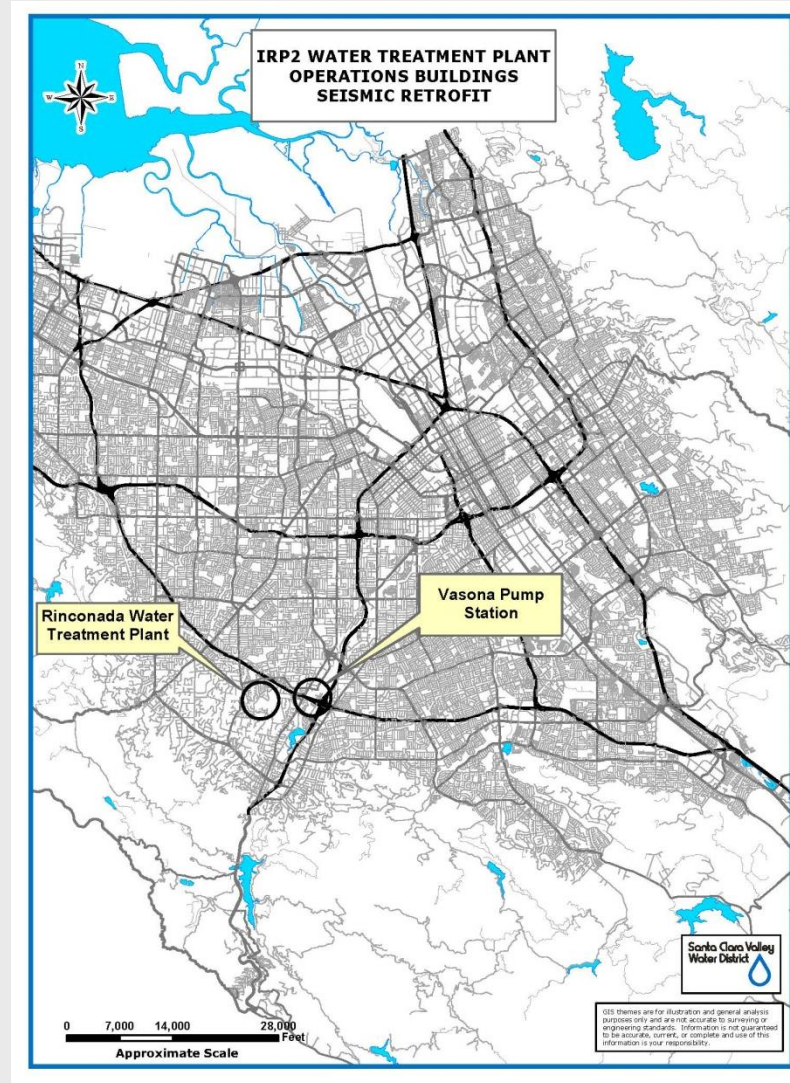

Presentation Topics

- ▶ Project Description, Objective, and Location
- ▶ Project Construction Costs
- ▶ Construction Photos



Project Costs

► Construction:

- \$8,367,000.00 – Contract Award Amount
- \$1,521,999.01 – Contract Change Orders
- \$9,888,999.01 – Final Contract Amount
(18 % increase)

► Funding Source:

- California OES Grant (\$703,867)
- Water Enterprise Fund – Zone W-2 (North County)



Presentation Topics

- ▶ Project Description, Objective, and Location
- ▶ Project Construction Costs
- ▶ Construction Photos



Construction Photos

B
E
F
O
R
E



A
F
T
E
R



Santa Clara Valley
Water District



Construction Photos

B
E
F
O
R
E



A
F
T
E
R



Santa Clara Valley
Water District

Attachment 4
Page 9 of 12



Construction Photos




Santa Clara Valley
Water District

Attachment 4
Page 10 of 12



Construction Photos

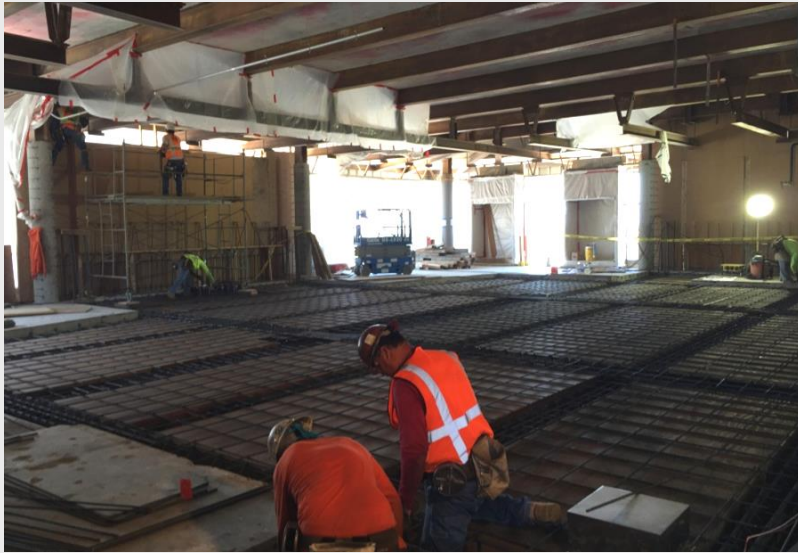

Santa Clara Valley
Water District



Attachment 4
Page 11 of 12

Construction Photos



Santa Clara Valley
Water District

