

# Lower Silver Creek Flood Protection and Creek Restoration Project, Reaches 5C to 6A

Notice of Completion of Construction Contract

November 28, 2017



# Presentation Topics

- ▶ Project Objective and Location
- ▶ Project Construction Costs
- ▶ Construction Photos




# Project Objective

The objective of the Lower Silver Creek Flood Protection and Creek Restoration Project is to:

- convey the 1-percent chance of flood flows and improve stream habitat values along 2.3 miles of the creek;
- together with future improvements planned by the District's Lake Cunningham project, provide flood protection for a total of 3,800 parcels in the surrounding area.



# Project Location

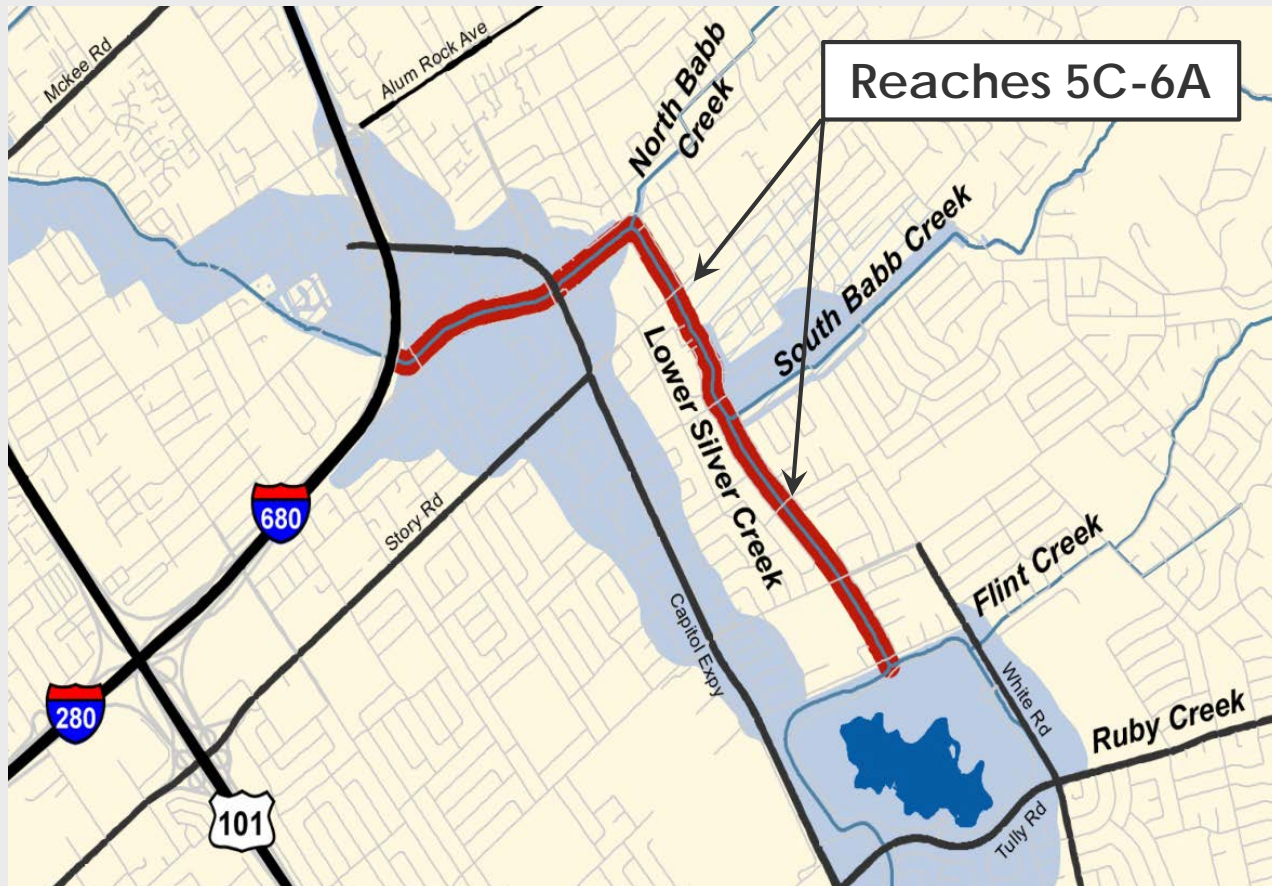

Santa Clara Valley  
Water District



# Presentation Topics

- ▶ Project Description, Objective, and Location
- ▶ Project Construction Costs
- ▶ Construction Photos



# Project Costs

## ▶ Construction:

- ▶ \$18,217,915.50 – Contract Award Amount
- ▶ \$ 2,727,359.43 – Contract Change Orders
- ▶ \$20,945,274.93 – Final Contract Amount  
(15% increase)

## ▶ Funding Source:

- ▶ Watershed Stream Stewardship Fund



# Presentation Topics

- ▶ Project Description, Objective, and Location
- ▶ Project Construction Costs
- ▶ Construction Photos





# Construction Photos

Before



After

Lower Silver Creek – Story Road Box Culvert

Santa Clara Valley  
Water District



Attachment 4  
Page 8 of 12



# Construction Photos

Before



After

Lower Silver Creek – upstream Story Road

Santa Clara Valley  
Water District



Attachment 4  
Page 9 of 12

# Construction Photos

Before



After

Lower Silver Creek – downstream Murtha Drive

Santa Clara Valley  
Water District



Attachment 4  
Page 10 of 12



# Construction Photos

Before



After

Lower Silver Creek – upstream Murtha Drive

Santa Clara Valley  
Water District



Attachment 4  
Page 11 of 12

# Construction Photos

Before



After

Lower Silver Creek – downstream Moss Point Drive

Santa Clara Valley  
Water District



Attachment 4  
Page 12 of 12
