

# Lower Silver Creek Flood Protection and Creek Restoration Project, Reach 6B

Notice of Completion of Construction Contract

August 14, 2018



# Presentation Topics

- ▶ Project Objective and Location
- ▶ Project Construction Costs
- ▶ Construction Photos




# Project Objective

The objective of the Lower Silver Creek Flood Protection and Creek Restoration Project is to:

- Convey the 1-percent flood flows and improve stream habitat values along 2.3 miles of the creek;
- Provide flood protection (upon completion of the District's Lake Cunningham Project) to a total of 3,800 parcels in the surrounding area.



# Project Location

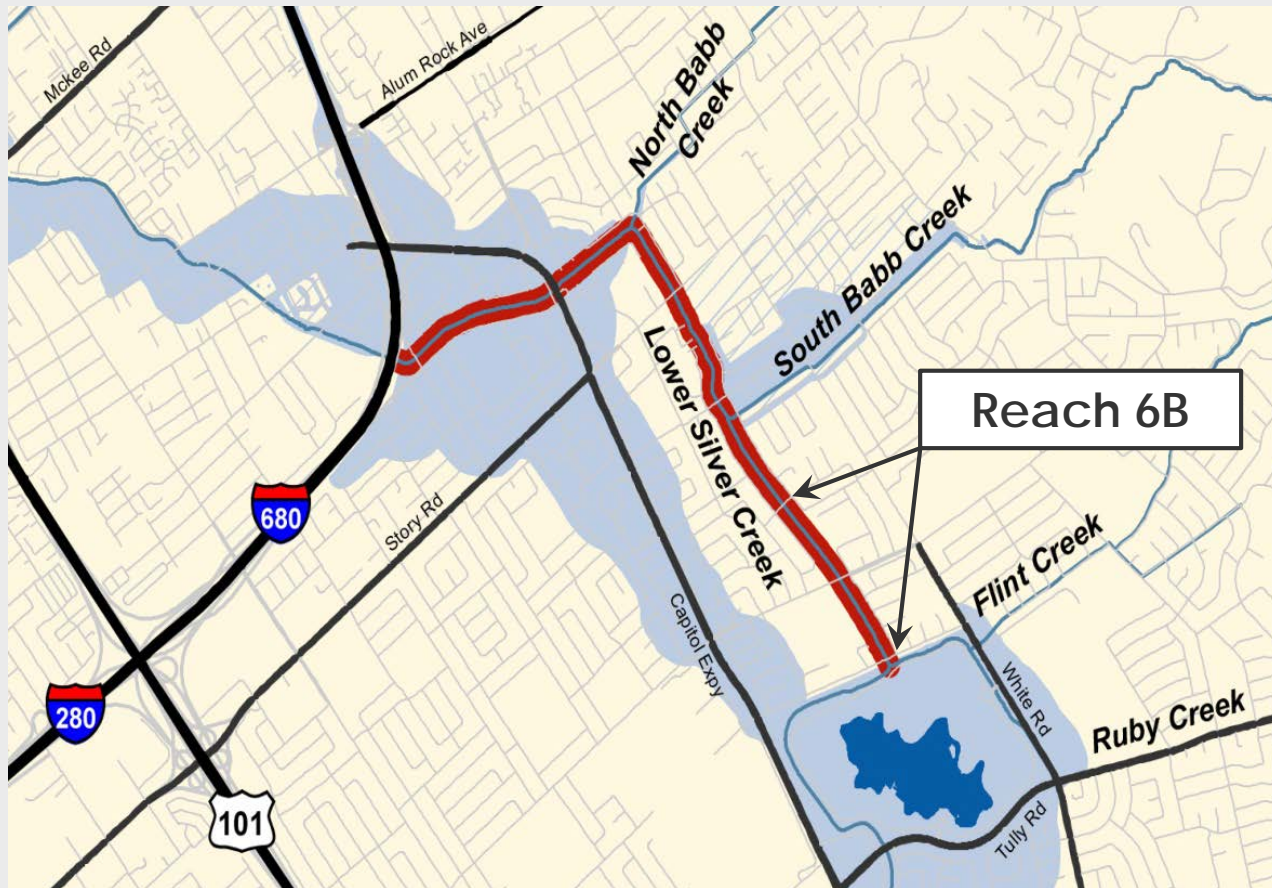

Santa Clara Valley  
Water District



# Presentation Topics

- ▶ Project Description, Objective, and Location
- ▶ Project Construction Costs
- ▶ Construction Photos



# Project Costs

## ► Construction:

- \$12,677,594.00 – Contract Award Amount
- \$ 1,097,329.43 – Contract Change Orders
- \$13,774,923.43 – Final Contract Amount  
(8.7% increase)

## ► Funding Sources:

- Watershed Stream Stewardship Fund
- Federal grant from Natural Resources Conservation Service



# Presentation Topics

- ▶ Project Description, Objective, and Location
- ▶ Project Construction Costs
- ▶ Construction Photos



# Construction Photos

Before



After

Lower Silver Creek – upstream Moss Point Drive

Santa Clara Valley  
Water District



Attachment 4  
Page 8 of 10

# Construction Photos

Before



After

Lower Silver Creek – downstream Ocala Avenue

Santa Clara Valley  
Water District



Attachment 4  
Page 9 of 10

# Construction Photos

Before



After

Lower Silver Creek – upstream of Ocala Avenue

Santa Clara Valley  
Water District



Attachment 4  
Page 10 of 10
